



PT. INSPEKTINDO SINERGI PERSADA




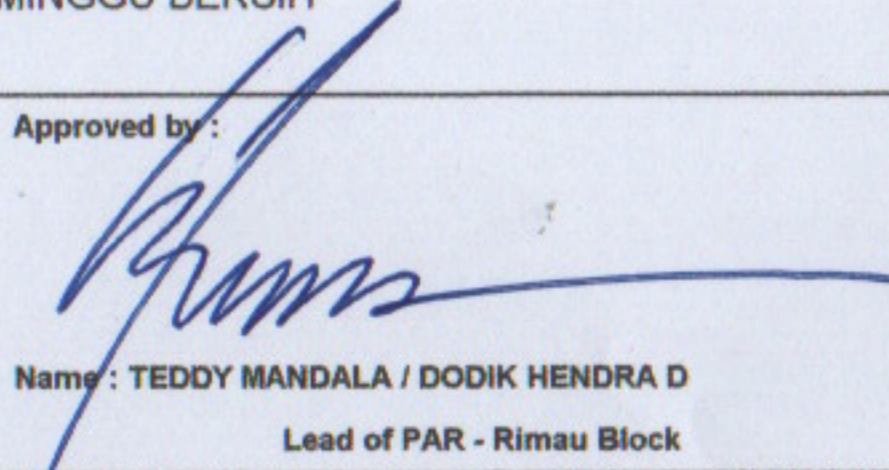
SERVICE TIMESHEET PAR

PT. Medco E & P

Contract Number : 3510007418

Location : Rimau Blok

Periode : 21 - 27 AGUSTUS 2023

| No. | Descriptions | UOM | Aug-23 | | | | | | | Total | | Job Description | | |
|---|--|----------|----------------------|----|---------|----------------------|---------------|----|----|-------|---|---|------------------------|---|
| | | | 21 | 22 | 23 | 24 | 25 | 26 | 27 | | | | | |
| 1 | Jasa Radiografi Test | Days | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 7 | Monday (21/08/23) | STAND BY DI KAJI | | |
| 2 | Jasa Dye Penetrant Test | Joints | - | 8 | 2 | 5 | - | - | - | 15 | | | | |
| 3 | Jasa Ultrasonic Test | Days | | | | | | | | 0 | | | | |
| 4 | Jasa Magnetic Particle Test | Days | | | | | | | | 0 | | | Tuesday (22/08/23) | 1. Dye Penetrant Test & Radiography Test Line Gas Compressor Semoga Stasiun 2. Dye Penetrant Test & Radiography Test Spool By Pass PGCU Semoga 3. Radiography Test Trunkline WI 8" Cluster I-L 4. Radiography Test Trunkline 8" Cluster B-BC 5. Radiography Test Trunkline 8" Cluster AI-AJ |
| 5 | Jasa Holiday Test | Days | | | | | | | | 0 | | | | |
| 6 | Jasa Hydrotest Pipeline/Flowline * Prehydrotest dilakukan oleh Perusahaan | AU | | | | | | | | 0 | | | Wednesday (23/8/23) | 1. Dye Penetrant Test & Radiography Test Flowline Gas 2" KS#93 Cluster V 2. Radiography Test Trunkline 8" Cluster B-BC 3. Radiography Test Trunkline 8" Cluster AI-AJ |
| 7 | Jasa Hydrotest Pipeline/Flowline * Prehydrotest dilakukan oleh Kontraktor | AU | | | | | | | | 0 | | | | |
| 8 | Hydrotest Piping system dalam station | AU | | | | | | | | 0 | | | | |
| 9 | Jasa Sewa Perahu Motor | Days | | | | | | | | 0 | | | Thursday (24/08/23) | 1. Dye Penetrant Test & Radiography Test Trunkline 8" Belakang EOR 2. Radiography Test Trunkline WI 8" Cluster I-L |
| Consumable Usage Summary | | | | | | | | | | | | | | |
| No. | DESCRIPTION | UOM | Aug-23 | | | | | | | Total | | | | |
| 1 | Film 4x10" | EA | - | 27 | 8 | - | 33 | - | - | 68 | Friday (25/08/23) | 1. Radiography Test Spool Gas Lipt 2" Cluster AE 2. Radiography Test Line Test 4" Cluster A | | |
| 2 | Film 4x15" | EA | - | 22 | 6 | 17 | - | 15 | - | 60 | | | | |
| Personnel | | | | | | | | | | | Saturday (26/08/23) | 1. Radiography Test Trunkline 8" Cluster AI, AJ 2. Radiography Test Trunkline 8" Cluster B, BC | | |
| No. | Name | Position | Working Period | | Remarks | | | | | | | | | |
| 1 | ANSYORI | PPR | 21 - 27 AGUSTUS 2023 | | 7 Day | | | | | | | | | |
| 2 | PETRUS HARRY NATALDO | OR/MT/PT | 21 - 27 AGUSTUS 2023 | | 7 Day | | | | | | | | | |
| 3 | MARWAN | OR/MT/PT | 21 - 27 AGUSTUS 2023 | | 7 Day | | | | | | | | | |
| 4 | AKBAR | ADM | 21 - 27 AGUSTUS 2023 | | 7 Day | | | | | | | | | |
| 6 | DIDIT KURNIAWAN | DRIVER | 21 - 27 AGUSTUS 2023 | | 4 Day | | | | | | | | | |
| 7 | RIKI SAPUTRA | DRIVER | 21 - 27 AGUSTUS 2023 | | 3 Day | Sunday (27/08/23) | MINGGU BERSIH | | | | | | | |
| Prepared by :   | | | | | | | | | | | | | | |
| Reviewed by :  | | | | | | | | | | | Approved by :  | | | |
| Name : AKBAR PEKTINDO SINERGI PERSADA | | | | | | | | | | | Name : TEDDY MANDALA / DODIK HENDRA D | | | |
| Date: 27 AGUSTUS 2023 | | | | | | | | | | | Lead of PAR - Rimau Blok | | | |
| | | | | | | | | | | | Supervisor of PAR | | | |



PT. INSPEKTINDO SINERGI PERSADA
SERVICE TIMESHEET PAR
 PT. Medco E & P
 Contract Number : 3510007418
 Location : Rimau Blok

Periode : 28 - 31 AGUSTUS 2023


| No. | Descriptions | UOM | Aug-23 | | | | | | Total | | Job Description |
|---------------------------------|---|----------|----------------------|----|---------|----|--|--|-------|------------------------|--|
| | | | 28 | 29 | 30 | 31 | | | | | |
| 1 | Jasa Radiografi Test | Days | 1 | 1 | 1 | 1 | | | 4 | Monday (28/08/23) | 1. Dye Penetrant Test & Radiography Test Line Gas Compressor FGCU Semoga 2. Radiography Test Line WI 4" Cluster L |
| 2 | Jasa Dye Penetrant Test | Joints | 1 | - | - | 4 | | | 5 | | |
| 3 | Jasa Ultrasonic Test | Days | | | | | | | 0 | | |
| 4 | Jasa Magnetic Particle Test | Days | | | | | | | 0 | Tuesday (29/08/23) | 1. Radiography Test Spool Gas Lipt KS#237 Cluster O 2. Radiography Test Line WI 4" Cluster L |
| 5 | Jasa Holiday Test | Days | | | | | | | 0 | | |
| 6 | Jasa Hydrotest Pipeline/Flowline <i>* Prehydrotest dilakukan oleh Perusahaan</i> | AU | | | | | | | 0 | Wednesday (30/8/23) | 1. Radiography Test Trunkline 8" Cluster B-BC 2. Radiography Test Line WI 4" Cluster L |
| 7 | Jasa Hydrotest Pipeline/Flowline <i>* Prehydrotest dilakukan oleh Kontraktor</i> | AU | | | | | | | 0 | | |
| 8 | Hydrotest Piping system dalam station | AU | | | | | | | 0 | | |
| 9 | Jasa Sewa Perahu Motor | Days | | | | | | | 0 | Thursday (31/08/23) | 1. Dye Penetrant Test & Radiography Test Line WI 4" Cluster L Tahap 2 2. Radiography Test Line Test Clamp |
| Consumable Usage Summary | | | | | | | | | | | |
| No. | DESCRIPTION | UOM | Aug-23 | | | | | | Total | | |
| 1 | Film 4x10" | EA | 27 | 27 | 28 | 24 | | | | 106 | |
| 2 | Film 4x15" | EA | - | - | 6 | - | | | | 6 | |
| Personnel | | | | | | | | | | | |
| No. | Name | Position | Working Period | | Remarks | | | | | | |
| 1 | AKBAR | ADMIN | 28 - 31 AGUSTUS 2023 | | 4 Day | | | | | | |
| 2 | ANSYORI | PPR | 28 - 31 AGUSTUS 2023 | | 4 Day | | | | | | |
| 3 | PETRUS HARRY NATALDO | OR/MT/PT | 28 - 31 AGUSTUS 2023 | | 4 Day | | | | | | |
| 4 | MARWAN | OR/MT/PT | 28 - 31 AGUSTUS 2023 | | 4 Day | | | | | | |
| 5 | RIKI SAPUTRA | DRIVER | 28 - 31 AGUSTUS 2023 | | 4 Day | | | | | | |


Prepared by :

Reviewed by :

Approved by :


 Name : AKBAR PEKTIINDO SINERGI PERSADA


 Name : WILLIAM / EKA CHANDRA
 Supervisor of PAR



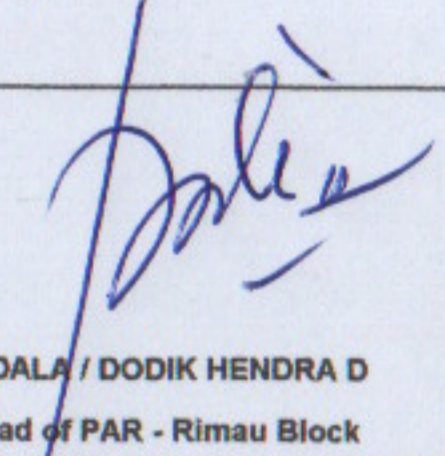

 Name : TEDDY MANDALA / DODIK HENDRA D
 Lead of PAR - Rimau Block




Date: 31 AGUSTUS 2023



PT. INSPEKTINDO SINERGI PERSADA
SERVICE TIMESHEET PAR
 PT. Medco E & P
 Contract Number : 3510007418
 Location : Rimau Blok

Periode : 01 - 03 SEPTEMBER 2023

| No. | Descriptions | UOM | Sep-23 | | | | | | Total | Job Description |
|---|---|--|------------------------|---------|---|----|----|----|-------|----------------------|
| | | | | | | 1 | 2 | 3 | | |
| 1 | Jasa Radiografi Test | Days | | | | 1 | 1 | 1 | 3 | |
| 2 | Jasa Dye Penetrant Test | Joints | | | | - | - | 3 | 3 | |
| 3 | Jasa Ultrasonic Test | Days | | | | | | | 0 | |
| 4 | Jasa Magnetic Particle Test | Days | | | | | | | 0 | |
| 5 | Jasa Holiday Test | Days | | | | | | | 0 | |
| 6 | Jasa Hydrotest Pipeline/Flowline <i>* Prehydrotest dilakukan oleh Perusahaan</i> | AU | | | | | | | 0 | |
| 7 | Jasa Hydrotest Pipeline/Flowline <i>* Prehydrotest dilakukan oleh Kontraktor</i> | AU | | | | | | | 0 | |
| 8 | Hydrotest Piping system dalam station | AU | | | | | | | 0 | |
| 9 | Jasa Sewa Perahu Motor | Days | | | | | | | 0 | |
| Consumable Usage Summary | | | | | | | | | | |
| No. | DESCRIPTION | UOM | Sep-23 | | | | | | Total | |
| 1 | Film 4x10" | EA | | | | 12 | 15 | 15 | 42 | Friday (01/09/23) |
| 2 | Film 4x15" | EA | | | | 12 | - | - | 12 | |
| Personnel | | | | | | | | | | |
| No. | Name | Position | Working Period | Remarks | | | | | | |
| 1 | FITER RONALD | COORDINATOR/AR | 01 - 03 SEPTEMBER 2023 | 3 Day | Saturday (02/09/23) | | | | | |
| 2 | ANSYORI | PPR | 01 - 03 SEPTEMBER 2023 | 3 Day | | | | | | |
| 3 | PETRUS HARRY NATALDO | OR/MT/PT | 01 - 03 SEPTEMBER 2023 | 3 Day | | | | | | |
| 4 | MARWAN | OR/MT/PT | 01 - 03 SEPTEMBER 2023 | 3 Day | | | | | | |
| 5 | AKBAR | ADM | 01 - 03 SEPTEMBER 2023 | 3 Day | | | | | | |
| 6 | RIKI SAPUTRA | DRIVER | 01 - 03 SEPTEMBER 2023 | 3 Day | | | | | | |
| | | | | | Sunday (03/09/23) | | | | | |
| | | | | | 1. Radiography Test Line WI 4" Cluster L Line B 2. Radiography Test Trunkline 8" Cluster AI-AJ | | | | | |
| | | | | | 1. Radiography Test Line Bypass Pump Transfer Kaji Satelit | | | | | |
| | | | | | 1. Radiography Test Line WI 4" Cluster L Line B 2. Dye Penetrant Test Line Bypass Pump Transfer Kaji Satelit | | | | | |
| Prepared by :  | | Reviewed by :  | | | Approved by :  | | | | | |
| Name : AKBAR INSPEKTINDO SINERGI PERSADA | | Name : WILLIAM EKA CHANDRA Supervisor of PAR | | | Name : TEDDY MANDALA / DODIK HENDRA D Lead of PAR - Rimau Block | | | | | |
| Date: 03-Sep-23 | | | | | | | | | | |

| No. | Descriptions | UOM | Sep-23 | | | | | | | Total | | Job Description | | |
|---|--|----------------|------------------------|---------|---|----|----|----|----|-------|---|--|---|--|
| | | | 4 | 5 | 6 | 7 | 8 | 9 | 10 | | | | | |
| 1 | Jasa Radiografi Test | Days | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 7 | Monday (04/09/23) | 1. Radiography Test Line Bypass Pump Transfer Kaji Satelit 2. Radiography Test Spool Gas Lipt 2" KS#237 Cluster O | | |
| 2 | Jasa Dye Penetrant Test | Joints | - | 2 | - | - | 2 | 10 | 3 | 17 | | | | |
| 3 | Jasa Ultrasonic Test | Days | | | | | | | | 0 | Tuesday (05/09/23) | 1. Radiography Test & Dye Penetrant Test Line WI 4" Cluster L Line B 2. Radiography Test Trunkline 8" Cluster AI-AJ & Cluster B-BC 3. Radiography Test Line Fider 4" & 6" Wash Tank Semoga | | |
| 4 | Jasa Magnetic Particle Test | Days | | | | | | | | 0 | | | | |
| 5 | Jasa Holiday Test | Days | | | | | | | | 0 | Wednesday (06/09/23) | 1. Radiography Test Line Test 4" Cluster A | | |
| 6 | Jasa Hydrottest Pipeline/Flowline * Prehydrottest dilakukan oleh Perusahaan | AU | | | | | | | | 0 | | | | |
| 7 | Jasa Hydrottest Pipeline/Flowline * Prehydrottest dilakukan oleh Kontraktor | AU | | | | | | | | 0 | Thursday (07/09/23) | 1. Radiography Test Line Test 4" Cluster A 2. Radiography Test Spool Gas Lipt 2" KS#237 Cluster O 3. Radiography Test Line Fider 4" & 6" Wash Tank Semoga | | |
| 8 | Hydrottest Piping system dalam station | AU | | | | | | | | 0 | | | | |
| 9 | Jasa Sewa Perahu Motor | Days | | | | | | | | 0 | Friday (08/09/23) | 1. Radiography Test & Dye Penetrant Test Trunkline WI 4" Cluster AP 2. Radiography Test Line WI 4" Cluster L Line B 3. Radiography Test Line Fider 4" & 6" Wash Tank Semoga | | |
| Consumable Usage Summary | | | | | | | | | | | | | | |
| No. | DESCRIPTION | UOM | Sep-23 | | | | | | | Total | | | | |
| 1 | Film 4x10" | EA | 15 | 42 | 9 | 22 | 30 | 2 | 24 | 144 | Saturday (09/09/23) | 1. Radiography Test & Dye Penetrant Test Line Test 4" dan Slip On Cluster A | | |
| 2 | Film 4x15" | EA | - | 15 | - | - | - | - | - | 15 | | | | |
| Personnel | | | | | | | | | | | Sunday (10/09/23) | 1. Radiography Test & Dye Penetrant Test Line Fider Wash Tank Semoga 2. Dye Penetrant Test Trunkline WI 4" Cluster AP | | |
| No. | Name | Position | Working Period | Remarks | | | | | | | | | | |
| 1 | FITER RONALD | COORDINATOR/AR | 04 - 10 SEPTEMBER 2023 | 7 Day | | | | | | | | | | |
| 2 | ANSYORI | PPR | 04 - 10 SEPTEMBER 2023 | 7 Day | | | | | | | | | | |
| 3 | PETRUS HARRY NATALDO | OR/MT/PT | 04 - 10 SEPTEMBER 2023 | 3 Day | | | | | | | | | | |
| 4 | MARWAN | OR/MT/PT | 04 - 10 SEPTEMBER 2023 | 7 Day | | | | | | | | | | |
| 5 | AKBAR | ADM | 04 - 10 SEPTEMBER 2023 | 7 Day | | | | | | | | | | |
| 6 | RIKI SAPUTRA | DRIVER | 04 - 10 SEPTEMBER 2023 | 7 Day | | | | | | | | | | |
| 7 | ANDY ANTONY | AR | 04 - 10 SEPTEMBER 2023 | 4 Day | | | | | | | | | | |
| Prepared by : | | | | | | | | | | | Reviewed by : | | Approved by : | |
|  Name : AKBAR PEKTINDO SINERGI PERSADA Date: 10-Sep-23 | | | | | | | | | | |  Name : WILLIAM / EKA CHANDRA Supervisor of PAR | |  Name : TEDDY MANDALA / DODIK HENDRA D Lead of PAR - Rimau Block | |

Inspection Services

| No. | Descriptions | UOM | September 2023 | | | | | | | Total | Job Description |
|---------------------------------|---|-------------------|------------------------|---|---------|--|----|----|----|-------|---|
| | | | 4 | 5 | 6 | 7 | 8 | 9 | 10 | | |
| 1 | Jasa Radiografi Test | Days | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 7 | Monday 1. Radiography Test : Standby Waiting Request for Radiography ✓ |
| 2 | Jasa Dye Penetrant Test | Joints | | | | | | | | 0 | |
| 3 | Jasa Ultrasonic Test | | | | | | | | | 0 | |
| 4 | Jasa Magnetic Particle Test | Days | | | | | | | | 0 | Tuesday 1. Radiography Test : Standby Waiting Request for Radiography ✓ |
| 5 | Jasa Holiday Test | Days | | | | | | | | 0 | |
| 6 | Jasa Hydrotest Pipeline/Flowline <i>* Prehydrotest dilakukan oleh Perusahaan</i> | AU | | | | | | | | 0 | Wednesday 1. Radiography Test line Produksi Satelit Jene Ø 8" = 7 Joint (21 Sheet) ✓ 2. Radiography Test Mainline Cobinasi Group A to B Jene Ø 6" = 1 Joint (3 Sheet) ✓ |
| 7 | Jasa Hydrotest Pipeline/Flowline <i>* Prehydrotest dilakukan oleh Kontraktor</i> | AU | | | | | | | | 0 | |
| 8 | Hydrotest Piping system dalam station | AU | | | | | | | | 0 | |
| 9 | Jasa Sewa Perahu Motor | Days | | | | | | | | 0 | Thursday 1. Radiography Test : Standby Waiting Request for Radiography ✓ |
| Consumable Usage Summary | | | | | | | | | | | |
| No. | DESCRIPTION | UOM | September 2023 | | | | | | | Total | Job Description |
| | | | 4 | 5 | 6 | 7 | 8 | 9 | 10 | | |
| 1 | Film 4x10" | EA | 0 | 0 | 3 | 0 | 40 | 0 | 47 | 90 | Friday 1. Radiography Test Ibul Optimization WIP Ibul 03 Ø 2" = 2 Joint (4 Sheet) ✓ Ø 3" = 2 Joint (6 Sheet) ✓ Ø 4" = 6 Joint (18 Sheet) ✓ Ø 6" = 4 Joint (12 Sheet) ✓ Ø 3" = 2 Joint (6 Sheet) ✓ |
| 2 | Film 4x15" | EA | 0 | 0 | 21 | 0 | 6 | 39 | 0 | 66 | |
| Personnel | | | | | | | | | | | |
| No. | Name | Position | Working Period | | Remarks | Saturday 1. Radiography Test line Produksi Satelit Jene Ø 8" = 13 Joint (39 Sheet) ✓ | | | | | |
| 1 | Zulfi Irfandi | SITE COORDINATOR | 04 - 10 September 2023 | | 7 Days | | | | | | |
| 2 | Forsanto Tambun | AR / MTPT Lev II | 04 - 10 September 2023 | | 7 Days | | | | | | |
| 3 | Nauval Iqbal | PPR / MTPT Lev II | 04 - 10 September 2023 | | 7 Days | | | | | | |
| 4 | Bayu Prasetyo | OR / MTPT Lev II | 04 - 10 September 2023 | | 7 Days | | | | | | |
| 5 | Petrus N N | OR | 04 - 10 September 2023 | | 7 Days | | | | | | |
| 6 | Dedek Candra P | Driver | 04 - 10 September 2023 | | 7 Days | Sunday 1. Radiography Test Replacement Mainline Fariz Ø 6" = 22 Joint (47 Sheet) ✓ | | | | | |

Prepared by:



Name : Zulfi Irfandi

Dated : 10-Sep-23

Approved by:





Name : Dodi.S / Yayan.S / Joko T

Dated :

Inspection Services

Periode : 11 s.d 17 Sept 2023

| No. | Descriptions | UOM | September 2023 | | | | | | | Total | Job Description |
|--|---|-------------------|------------------------|----|---------|--|--|----|----|-------|--|
| | | | 11 | 12 | 13 | 14 | 15 | 16 | 17 | | |
| 1 | Jasa Radiografi Test | Days | 1 | 1 | 1 | 1 | 1 | 1 | 1 | 7 | Monday 1. Radiography Test Replacement Mainline Fariz Ø 6" = 3 Joint (5 Sheet) ✓ |
| 2 | Jasa Dye Penetrant Test | Joints | | | 4 | 6 | | | | 10 | |
| 3 | Jasa Ultrasonic Test | Days | | | | | | | | 0 | |
| 4 | Jasa Magnetic Particle Test | Days | | | | | | | | 0 | Tuesday 1. Radiography Test Replacement Mainline Fariz Ø 6" = 4 Joint (6 Sheet) ✓ |
| 5 | Jasa Holiday Test | Days | | | | | | | | 0 | |
| 6 | Jasa Hydrotest Pipeline/Flowline <i>* Prehydrotest dilakukan oleh Perusahaan</i> | AU | | | | | | | | 0 | Wednesday 1. Radiography Test line Produksi Satelit Jene Ø 8" = 13 Joint 39 Sheet) ✓ 2. Radiography Test Re-Route Fuel Gas Line Jene Ø 3" = 1 Joint (3 Sheet) ✓ 3. Penetrant Test Re-Route Fuel Gas Line Jene = 4 Joint ✓ |
| 7 | Jasa Hydrotest Pipeline/Flowline <i>* Prehydrotest dilakukan oleh Kontraktor</i> | AU | | | | | | | | 0 | |
| 8 | Hydrotest Piping system dalam station | AU | | | | | | | | 0 | |
| 9 | Jasa Sewa Perahu Motor | Days | | | | | | | | 0 | Thursday 1. Radiography Test Ibul Optimization WIP Ibul 03 Ø 2" = 2 Joint (4 Sheet) ✓ Ø 6" = 1 Joint (3 Sheet) ✓ Ø 8" = 9 Joint (25 Sheet) ✓ |
| Consumable Usage Summary | | | | | | | | | | | |
| No. | DESCRIPTION | UOM | September 2023 | | | | | | | Total | Job Description |
| | | | 11 | 12 | 13 | 14 | 15 | 16 | 17 | | |
| 1 | Film 4x10" | EA | 5 | 6 | 3 | 7 | 21 | 15 | 6 | 63 | Friday 1. Radiography Test Ibul Optimization WIP Ibul 03 Ø 2" = 3 Joint (6 Sheet) ✓ Ø 3" = 2 Joint (5 Sheet) ✓ Ø 4" = 3 Joint (7 Sheet) ✓ Ø 6" = 1 Joint (3 Sheet) ✓ |
| 2 | Film 4x15" | EA | 0 | 0 | 39 | 25 | 0 | 0 | 0 | 64 | |
| Personnel | | | | | | | | | | | |
| No. | Name | Position | Working Period | | Remarks | Saturday 1. Radiography Test Replacement Mainline Fariz Ø 6" = 10 Joint (15 Sheet) ✓ | | | | | |
| 1 | Zulfi Irfandi | SITE COORDINATOR | 11 - 17 September 2023 | | 7 Days | | | | | | |
| 2 | Forsanto Tambun | AR / MTPT Lev II | 11 - 17 September 2023 | | 7 Days | | | | | | |
| 3 | Nauval Iqbal | PPR / MTPT Lev II | 11 - 16 September 2023 | | 6 Days | | | | | | |
| 4 | M. Irfangi | PPR | 17 September 2023 | | 1 Days | | | | | | |
| 5 | Bayu Prasetyo | OR / MTPT Lev II | 11 - 17 September 2023 | | 7 Days | | | | | | |
| 6 | Petrus N N | OR | 11 - 17 September 2023 | | 7 Days | | | | | | |
| 7 | Dedek Candra P | Driver | 11 - 17 September 2023 | | 7 Days | Sunday 1. Radiography Test Replacement Mainline Fariz Ø 6" = 2 Joint (6 Sheet) ✓ | | | | | |
| Prepared by: | | | | | | | | | | | |
|  Name : Zulfi Irfandi Dated : 17-Sep-23 | | | | | | | Approved by:  Name : Dodi.S / Yayan.S / Joko T Dated : | | | | |

WEEKLY TIMESHEET

PT. Medco E & P

Contract Number : 3510007418

Location : SSB West & East

Inspection Services

Periode : 18 s.d 20 Sept 2023

| No. | Descriptions | UOM | September 2023 | | | | | | | Total | Job Description |
|-----|---|--------|----------------|----|----|--|--|--|--|-------|---|
| | | | 18 | 19 | 20 | | | | | | |
| 1 | Jasa Radiografi Test | Days | 1 | 1 | 1 | | | | | 3 | Monday (18-09-2023) 1. Radiography Test Replacement Mainline Fariz Ø 6" = 4 Joint (5 Sheet) 2. Penetrant Test Chasis TMC Unit WMA = 3 Joint |
| 2 | Jasa Dye Penetrant Test | Joints | 3 | | | | | | | 3 | |
| 3 | Jasa Ultrasonic Test | Days | | | | | | | | 0 | |
| 4 | Jasa Magnetic Particle Test | Days | | | | | | | | 0 | Tuesday (19-09-2023) 1. Radiography Test Replacement Mainline Fariz Ø 6" = 3 Joint (9 Sheet) |
| 5 | Jasa Holiday Test | Days | | | | | | | | 0 | |
| 6 | Jasa Hydrotest Pipeline/Flowline <i>* Prehydrotest dilakukan oleh Perusahaan</i> | AU | | | | | | | | 0 | Wednesday (20-09-2023) 1. Radiography Test Replacement Mainline Fariz Ø 6" = 1 Joint (1 Sheet) |
| 7 | Jasa Hydrotest Pipeline/Flowline <i>* Prehydrotest dilakukan oleh Kontraktor</i> | AU | | | | | | | | 0 | |
| 8 | Hydrotest Piping system dalam station | AU | | | | | | | | 0 | |
| 9 | Jasa Sewa Perahu Motor | Days | | | | | | | | 0 | |


Consumable Usage Summary

| No. | DESCRIPTION | UOM | September 2023 | | | | | | | Total |
|-----|-------------|-----|----------------|----|----|--|--|--|--|-------|
| | | | 18 | 19 | 20 | | | | | |
| 1 | Film 4x10" | EA | 5 | 9 | 1 | | | | | 15 |
| 2 | Film 4x15" | EA | 0 | 0 | 0 | | | | | 0 |

Personnel

| No. | Name | Position | Working Period | Remarks |
|-----|-----------------|------------------|------------------------|---------|
| 1 | Zulfi Irfandi | SITE COORDINATOR | 18 - 20 September 2023 | 3 Days |
| 2 | Forsanto Tambun | AR / MTPT Lev II | 18 - 20 September 2023 | 3 Days |
| 3 | M. Irfangi | PPR | 18 - 20 September 2023 | 3 Days |
| 4 | Bayu Prasetyo | OR / MTPT Lev II | 18 - 20 September 2023 | 3 Days |
| 5 | Petrus Harry NN | OR / MTPT Lev II | 18 - 20 September 2023 | 3 Days |
| 6 | Dedek Candra P | Driver | 18 - 20 September 2023 | 3 Days |


Prepared by:



Name : Zulfi Irfandi

Dated : 24-Sep-23

Approved by:



Name : Dodi.S / Yayan.S / Joko T

Dated :
